

Attachment J

Sample Completed Grant Application

See next page for accompanying sketch

County/Twp - Indiana/Best SECTION 9106 OF THE PENNSYLVANIA VEHICLE CODE
 DIRT AND GRAVEL ROADS GRANT APPLICATION Date: 06/23/98
 Mailing Address: RD #1 Normal, PA 15777 Zip Code: 15777
 Phone: 724/397-1234 FAX: - B-Mail: -
 Road ID Number/Name: TR 457 / Toad Road.

Best Township
 Official Name of Applying Agency
 Woody Dorite
 Contact Person
 Unkn. Trib Cosh Creek
 Affected Stream or Tributary

1. List personnel who have received "Environmentally Sensitive Maintenance of Dirt and Gravel Roads" Training.

Bill Smith / Roadmaster - Supv. 1997 Year 1997 Name / Position Tom Turner / Equip. Operator 1997 Year 1997

2. Will the work involve floodplains, stream crossings, stream work or wetlands? Yes No
 If yes, list the Department of Environmental Protection permits that have been obtained or pending. Minor Road Crossing GP-073298101

3. Check all the conditions that exist in the proposed work area.
 Eroded ditches Inadequate stream crossings Lack of road crown
 Flooded road banks Inadequate cross pipes Poor base composition
 Discharges directly to stream Groundwater in road bed Excessive road sliding
 Stream bank erosion Excessive loss of road fines (dust) Ineffective vegetative buffers

4. Is this a previously verified work site? Yes No
 5. Do materials proposed to be used on the project meet State Conservation Commission conditions for non-polluting? Yes NA

List commercial products to be used for the project.
 6. On the back of the application include a sketch of the road with the proposed work elements. Include a photocopy of the topographic map with the work site highlighted.

7. Proposed start/completion date: 7-98 / 9-98 Check if project would be considered an emergency. IN Kind Contr. batten

8. Project cost summary:
 Materials Equip Labor Material Equip.
 Pipes # 1620 Rental \$ 600 Truck 1260 Trp. - 4/200 # 7324
 Fabric 630 Trp Grader 350
 Stone 3120 9996.2
4124
 Grant Requested \$ 6320 978
 In-kind contributions \$ 2460
 Total project cost \$ 8780 9784

W. Dorite
 Applicant Signature

Completed Project Sketch

Sketch should go on back of completed Grant Application from previous page

Materials

Pipes:

15" CPP - 180' x 5.00/ft = \$ 900.00
 48" Cpp - 30' x 24.00/ft = 720.00

Geotextile: 18' x 700' x .05/ft² = 630

Aggregate:


Inlet/outlet R-5 50 tons @ 10/ton = 500

Stream/Road Bank R-7 66 tons @ 10/ton = 660

Road 700' x 18' x 4" = 245 ton @ 8 = 1960

6.2
9RB

6" = 370 ton = 2964

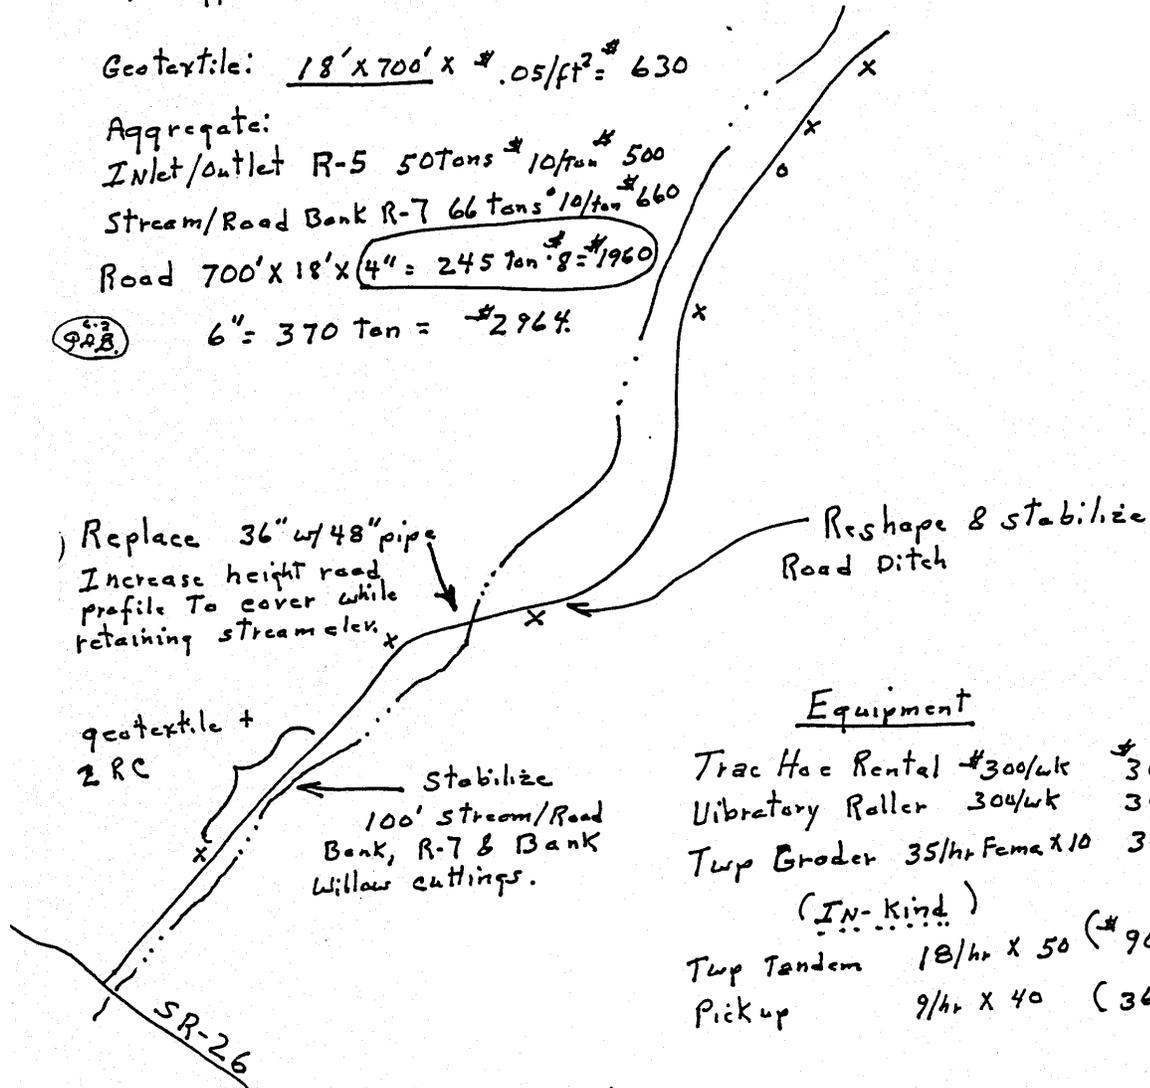

Replace 36" w/ 48" pipe
 Increase height road profile to cover while retaining stream elev.

Reshape & stabilize Road Ditch

geotextile + 2 RC

Stabilize 100' Stream/Road Bank, R-7 & Bank Willow cuttings.

Equipment

Trac Hac Rental \$300/wk \$ 300
 Vibratory Roller 304/wk 300
 Twp Grader 35/hr Fema x 10 350
 (IN-kind)
 Twp Tandem 18/hr x 50 (\$ 900)
 Pickup 9/hr x 40 (360)

LABOR (IN-kind)

120 Hours @ 10.00/hr. (1200)

Best Township Scale: 1" = 500'

o = Existing Crosspipes
 x = Proposed Crosspipes.
